DocID 5913

Source: Department of Ecology

(T-R-S) 27-4-20

(Q-Q) SE-SE

Site Address _____

Date Copied _____ By _____

- ❑ **Title page with the following information:**
  - o *Company (Author) name*
  - o *Report date*
  - o *Project Name*
  - o *Company's job number*
  - o *Site address*
- ❑ Executive Summary / Introduction of the report
- ❑ Table of contents
- ❑ Project Location Map / Vicinity Map
- ❑ **Site / Exploration Plans, Boring Location Plans**
- ❑ Cross-sections / Subsurface profiles
- ❑ **Exploration Logs**
- ❑ Monitoring Well Logs
- ❑ Cone Penetrometer Logs
- ❑ Groundwater Elevation Tables / Data

❑ Includes data from Previous Reports

❑ No new data / data review

❑ Missing Data / Illegible Data
Explanation _____

Comments: _____

1/1 (5913)

ENTERED

RESOURCE PROTECTION WELL REPORT

27/4/20R

START CARD NO. R27052

PROJECT NAME: KENS RADIATOR

WELL IDENTIFICATION NO. ACD 282

DRILLING METHOD: HSA

DRILLER: RODNEY LABROSSE

FIRM: Cascade Drilling, Inc.

SIGNATURE: Rodney Labrosse

CONSULTING FIRM: SECOR

REPRESENTATIVE: CLIFF SCHMITT

COUNTY: SNOHOMISH

LOCATION: SE 1/4 SE 1/4 Sec 20 Twn 27N R 4E

STREET ADDRESS OF WELL: [redacted] - LYNNWOOD

WATER LEVEL ELEVATION: 7'

GROUND SURFACE ELEVATION: N/A

INSTALLED: 12-21-95

DEVELOPED: YES

5530

AS-BUILT	WELL DATA	FORMATION DESCRIPTION
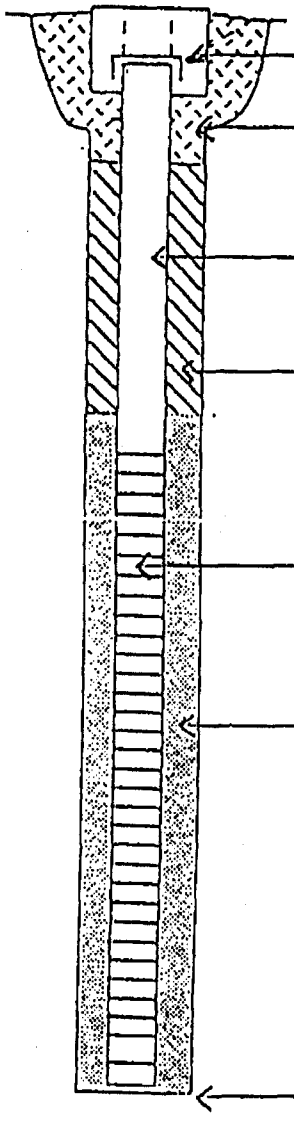	WELL COVER CONCRETE SURFACE SEAL DEPTH = 1/ft PVC BLANK 2" x 5' BACKFILL 1 ft. d TYPE: Bark chips PVC SCREEN 2" x 15' SLOT SIZE: 010 GRAVEL PACK 3 ft. d MATERIAL: #3 Lonester WELL DEPTH 20'	0 - 7 ft. brown silty w/ some sand 7 - 20 ft. till olive green and cobbles - ft.

RECEIVED
JAN 05 1996
DEPT. OF ECOLOGY

SCALE: 1" = _____

PAGE _____ OF _____

ECY 050-12 (Rev. 11/89)

D536 P536
